



"Everything in Excellence"

**WILLIAMS & THOMAS CONSTRUCTION CO.**

4473 Progress Ave., Ste 1, Naples, FL 34104

561.460.8525 | [www.wtconstruct.com](http://www.wtconstruct.com) | CGC1532780

**WEEKLY PROGRESS REPORT**

| Report No. | Date       |
|------------|------------|
| #15        | 12/02/2025 |

**CLIENT:**

**Huntington Lakes IV**

**7320 Amberly Lane, Delray Beach, FL 33446**

Attn: Nici Mahlandt | 201-936-9377

Email: [nmahlandt@hotmail.com](mailto:nmahlandt@hotmail.com)

**OWNER'S REP:**

**Hellas Engineering**

2475 Mercer Ave. Suite 106, West Palm Beach, Florida 33401

Contact: Austin Brennen 561-469-1907/561-348-4700

Email: [austin@hellaseng.com](mailto:austin@hellaseng.com)

**PROJECT: BUILDING RESTORATION PROJECT – HUNTINGTON LAKES IV**

**COMPLETED WORK BLDG WEEK ENDING Nov. 28**

**Monday, Nov. 24, 2025**

**Building 32** catwalks north elevation continuing with the post pocket repairs.

**Building 32** North elevation 3rd floor catwalk near unit #308 chipping area to engineer specs to get ready for concrete pour.

**Building 32** Northwest stairwell per engineer specs , for a through slab replace and repair add new and repair existing rebar.

**Building 32** South elevation framing area around post tension cables 5 to 7 days for stressing.

**Tuesday, Nov. 25, 2025**

**Building 32** Northwest stairwell make new rebar hooks for framing for the stairwell beam repairs.

**Building 32** Northwest stairwell finish framing and pour beam repairs.

**Building 32** North elevation strip concrete pours from previous week column repair pours.

**Building 32** South elevation paint all newly installed dens glass with waterproofing.

**Wednesday, Nov. 26, 2025**

**Building 32** Unit #304 Start window install framing in decent shape.

**Building 32** Unit #304 Clean and paint new framing with weatherproofing.

**Building 32** Unit #205 Start new window install framing in questionable shape a lot of rust.

**Building 32** Unit #205 Install new framing around window opening.

**Building 32** North elevation continue excavating last of the pockets on catwalk.

**Building 32** West elevation finish scaffolding on west elevation for unit #410 window install.

**Thursday, Nov. 27, 2025**

**Thanksgiving Day**



**Friday, Nov. 28, 2025**

**Building 32** Unit #410 starting window installation 5 windows going in.

**WEEKLY PROGRESS REPORT – SUMMARY DETAILS**

| WORK DAYS | Rain Day | Holiday | AVG. DAILY MANPOWER | BLDGS WORKING ON |
|-----------|----------|---------|---------------------|------------------|
| 4         | 0        | 1       | 6-8                 | 32               |

## WEEKLY PROGRESS REPORT #15

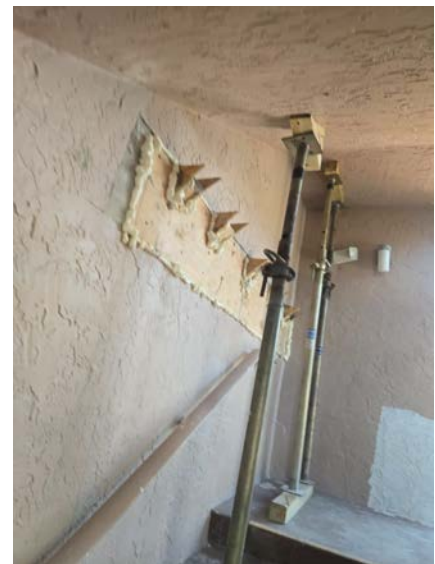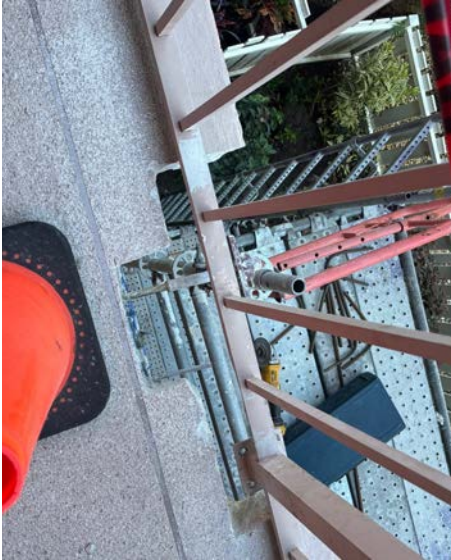

## WEEKLY PROGRESS REPORT #15

