



"Everything in Excellence"

WILLIAMS & THOMAS CONSTRUCTION CO.

4473 Progress Ave., Ste 1, Naples, FL 34104

561.460.8525 | www.wtconstruct.com | CGC1532780

WEEKLY PROGRESS REPORT

Report No.	Date
#36	04/24/26

CLIENT:

Huntington Lakes IV

7320 Amberly Lane, Delray Beach, FL 33446

Attn: Nici Mahlandt | 201-936-9377

Email: nmahlandt@hotmail.com

OWNER'S REP:

Hellas Engineering

2475 Mercer Ave. Suite 106, West Palm Beach, Florida 33401

Contact: Austin Brennen 561-469-1907/561-348-4700

Email: austin@hellaseng.com

PROJECT: BUILDING RESTORATION PROJECT — HUNTINGTON LAKES IV

Week of 4/20-4/24

Building 29 — Began work on lanais

Building 29 — Worked on interior lanais 3 and 4 stacks

Building 29 — Worked on interior lanais 2 and 3 stacks

Building 29 — Completed interior work in final stacks

Building 30 — Installed framing on units 105 and 205 on South elevation

Building 30 — Installed wire mesh on south elevation (10 stack) and other small patches around window 308-309-and 108.

Building 30 — Completed frame work with window installs in units 105 and 205

Building 30 — Finished Dens Glass installation on 105 and 205 w/Sto Gold weatherproofing

Building 30 — Cleaned rusted framing around units 104 and 204

Building 30 — Removed stucco in west stairwell for post tension cable location

Building 30 — New column excavations on 4th floor catwalk

Building 30 — Installed window framing and bucks in unit 204

Building 30 — Removed and installed plywood weather walls units 105/205

Building 30/31 — Inspections with Hellas engineer

Building 31 — Walked through units for interior punch out

Building 31 — Installed wire mesh for stucco on south elevation (1 stack)

Building 31 — Continued scratch coat on back wall of one stack

Building 32 — Removed EMSeal from expansion joint in center of building

OEC
MEETING
HELD
WEDNESDAY,
4/22


WEEKLY PROGRESS REPORT — SUMMARY DETAILS

WORK DAYS	WEATHER DELAYS	Holiday	AVG. DAILY MANPOWER	BLDGS WORKING ON
5	0	0	8-12	32/31/30/29

WEEKLY PROGRESS REPORT #36



Wire mesh installed.

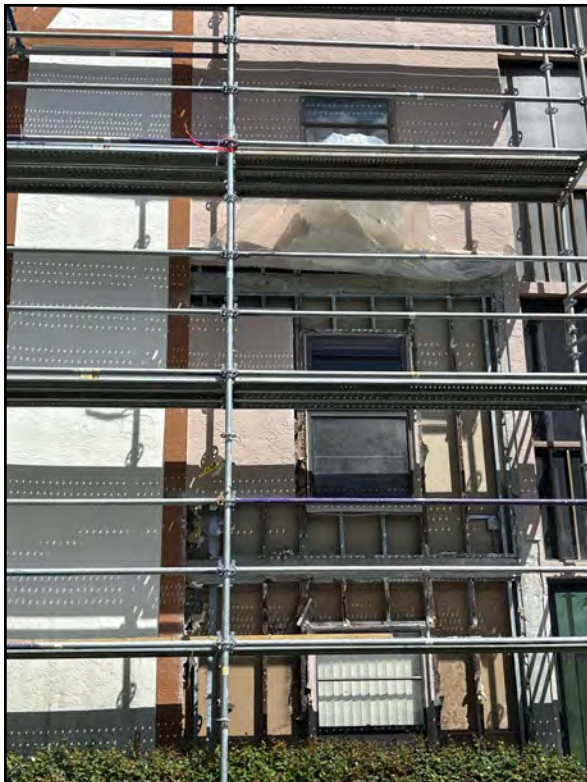


Window and frame repairs

WEEKLY PROGRESS REPORT #36




Dens Glass installation

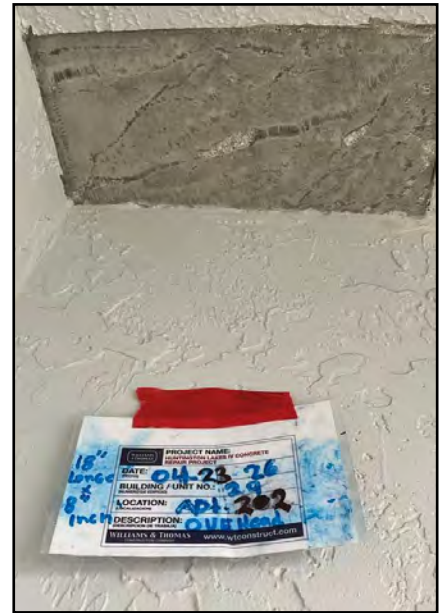

Interior repairs

WEEKLY PROGRESS REPORT #36

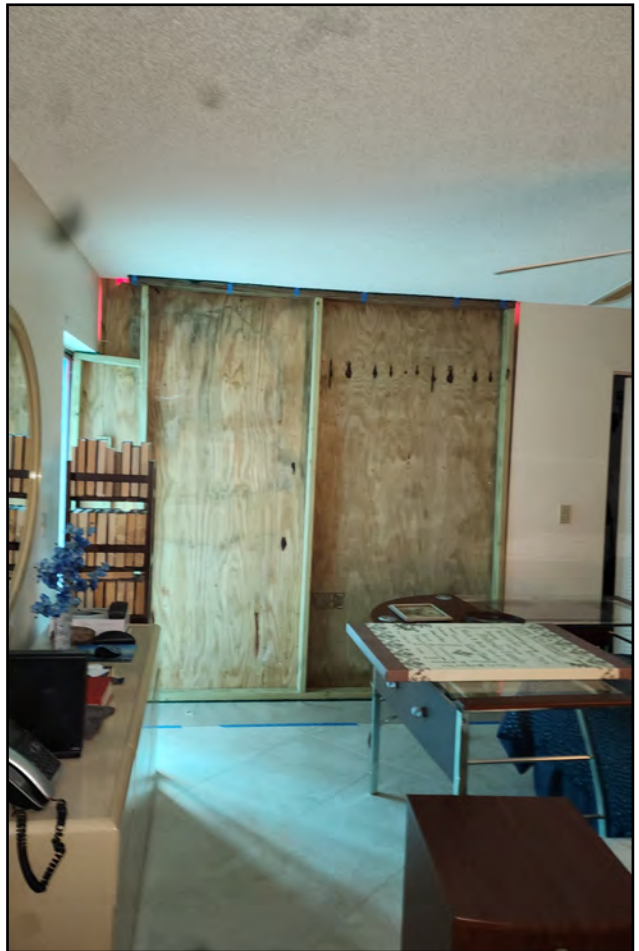

Plywood weather wall
