



"Everything in Excellence"

WILLIAMS & THOMAS CONSTRUCTION CO.

4473 Progress Ave., Ste 1, Naples, FL 34104

561.460.8525 | www.wtconstruct.com | CGC1532780

WEEKLY PROGRESS REPORT

Report No.	Date
#43	06/12/26

CLIENT:

Huntington Lakes IV

7320 Amberly Lane, Delray Beach, FL 33446

Attn: Nici Mahlandt | 201-936-9377

Email: nmahlandt@hotmail.com

OWNER'S REP:

Hellas Engineering

2475 Mercer Ave. Suite 106, West Palm Beach, Florida 33401

Contact: Austin Brennen 561-469-1907/561-348-4700

Email: austin@hellaseng.com

PROJECT: BUILDING RESTORATION PROJECT — HUNTINGTON LAKES IV

WEEK ENDING JUNE 12, 2026

Building 30

1. Framing on unit 301 and 101
2. Window bucking on unit 301 and 201
3. Added foam in pockets on fourth floor
4. Removed scaffolding from east side
5. Added control joints to stack 10
6. Poured grout in pockets
7. **SATURDAY — Post tension work**
 1. 30 — stressing cables third floor
 2. 32 — distressing cables by elevator
 3. 30 — Prepping stack 2 for stressing
8. Poured grout in some of the pockets on in the west staircase

Building 31

9. Continued engineer inspections on lanais

Building 29

10. Added scaffolding to back wall
11. Removed and installed new framing unit 310
12. Removed stucco

**Expected
Progress week
of 6/15/26**

**Begin lanai
inspections for
building 29**

**Identify post tension
cables in building 29**

Begin picket repairs

**Continue installation
of control joints on
EFIS walls**

**Stucco walls on
building 30**

**Continue window
installs on building 29**

WEEKLY PROGRESS REPORT — SUMMARY DETAILS

WORK DAYS	WEATHER DELAYS	Holiday	AVG. DAILY MANPOWER	BLDGS WORKING ON
5	0	0	10-13	30/31/29



"Everything in Excellence"


WILLIAMS & THOMAS CONSTRUCTION CO.

4473 Progress Ave., Ste 1, Naples, FL 34104

561.460.8525 | www.wtconstruct.com | CGC1532780

WEEKLY PROGRESS REPORT

Report No.	Date
#43	06/12/26

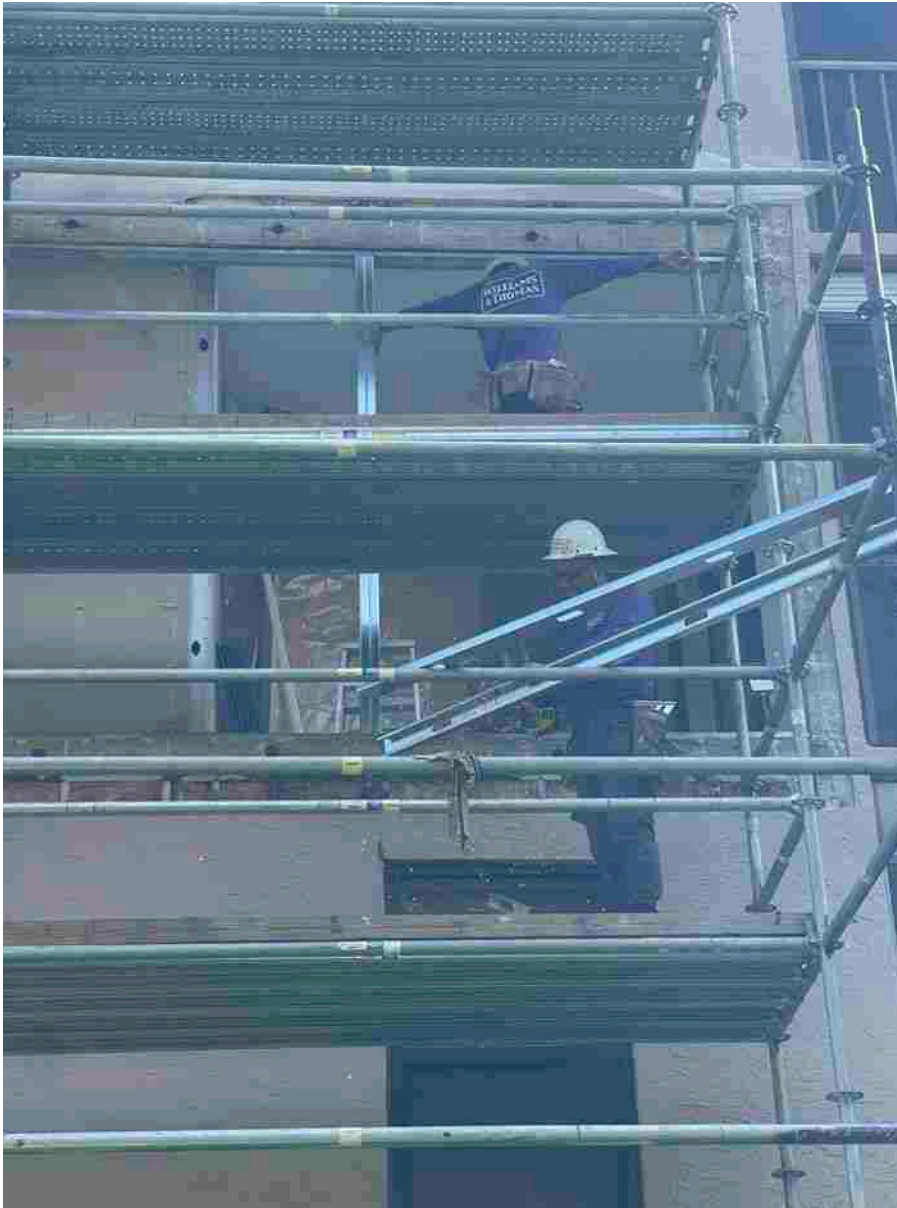

**Wall removed on 29/310.
Dust wall installed. New
framing installed.**





"Everything in Excellence"

WILLIAMS & THOMAS CONSTRUCTION CO.

4473 Progress Ave., Ste 1, Naples, FL 34104

561.460.8525 | www.wtconstruct.com | CGC1532780

WEEKLY PROGRESS REPORT

Report No.	Date
#43	06/12/26




Added additional scaffolding to building 29

Added control joints on back of building 30



Poured grout in west stairwell railing pockets.

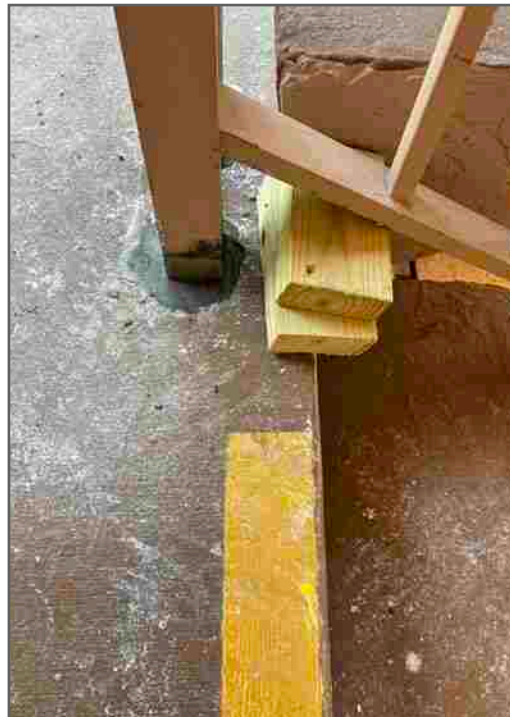



WILLIAMS & THOMAS CONSTRUCTION CO.
4473 Progress Ave., Ste 1, Naples, FL 34104
561.460.8525 | www.wtconstruct.com | CGC1532780

"Everything in Excellence"

CLIENT:

Huntington Lakes IV

7320 Amberly Lane, Delray Beach, FL 33446

Attn: Nici Mahlandt | 201-936-9377

Email: nmahlandt@hotmail.com

WEEKLY PROGRESS REPORT

Report No.	Date
#43	06/5/26

OWNER'S REP:

Hellas Engineering

2475 Mercer Ave. Suite 106, West Palm Beach, Florida 33401

Contact: Austin Brennen 561-469-1907/561-348-4700

Email: austin@hellaseng.com



Bad wall on stack 1.



**Post tension cable repairs/
replacements building 30
Stack 1**
