



"Everything in Excellence"

WILLIAMS & THOMAS CONSTRUCTION CO.

4473 Progress Ave., Ste 1, Naples, FL 34104

561.460.8525 | www.wtconstruct.com | CGC1532780

WEEKLY PROGRESS REPORT

Report No.	Date
#44	06/19/26

CLIENT:

Huntington Lakes IV

7320 Amberly Lane, Delray Beach, FL 33446

Attn: Nici Mahlandt | 201-936-9377

Email: nmahlandt@hotmail.com

OWNER'S REP:

Hellas Engineering

2475 Mercer Ave. Suite 106, West Palm Beach, Florida 33401

Contact: Austin Brennen 561-469-1907/561-348-4700

Email: austin@hellaseng.com

PROJECT: BUILDING RESTORATION PROJECT – HUNTINGTON LAKES IV

WEEK ENDING JUNE 19, 2026

Building 30

1. Control joints added to stacks 10 and 5. Need inspections on Monday.
2. Chipping of post pockets on 2nd, 3rd and 4th floors
8. DensGlass installed on units 303, 101, 201
9. Filled partial depth openings on west stairwell
10. Post tension repair stack 2

Building 31

11. Replaced corroded railing brackets
12. Cleaned storage unit floors
13. Poured concrete storage room floors

Building 29

14. Installed dust wall unit 110
15. Removed stucco and framing on unit 210
16. Removed and reinstalled window in unit 210

Building 32

17. Post tension cable lock offs by elevator

**Expected
Progress week
of 6/22/26**

**Begin lanai
inspections for
buildings 29 and 30**

**Continue EFIS repairs
on building 29
10 stack**


**Installation of control
joints on EFIS walls**

**Complete EFIS wall
installation upon
control joint approvals**

**Complete prep work
for Post Tension
repairs on building 32**

WEEKLY PROGRESS REPORT – SUMMARY DETAILS

WORK DAYS	WEATHER DELAYS	Holiday	AVG. DAILY MANPOWER	BLDGS WORKING ON
5	0	0	10-13	30/31/29



"Everything in Excellence"

WILLIAMS & THOMAS CONSTRUCTION CO.

4473 Progress Ave., Ste 1, Naples, FL 34104

561.460.8525 | www.wtconstruct.com | CGC1532780

WEEKLY PROGRESS REPORT

Report No.	Date
#44	06/19/26



**New framing on
Building 29, units 101,
201, 301**

**Post tension anchor repair
building 30 stack 2**



**Locking off
cables on
building 32
by elevator**

Report No.	Date
#44	06/19/26



**Control joints
installed —
waiting for
inspection.**



**Dens Glass
installation**






WILLIAMS & THOMAS CONSTRUCTION CO.
4473 Progress Ave., Ste 1, Naples, FL 34104
561.460.8525 | www.wtconstruct.com | CGC1532780

WEEKLY PROGRESS REPORT	
Report No.	Date
#44	06/19/26



Cleaned storage unit floors building 31

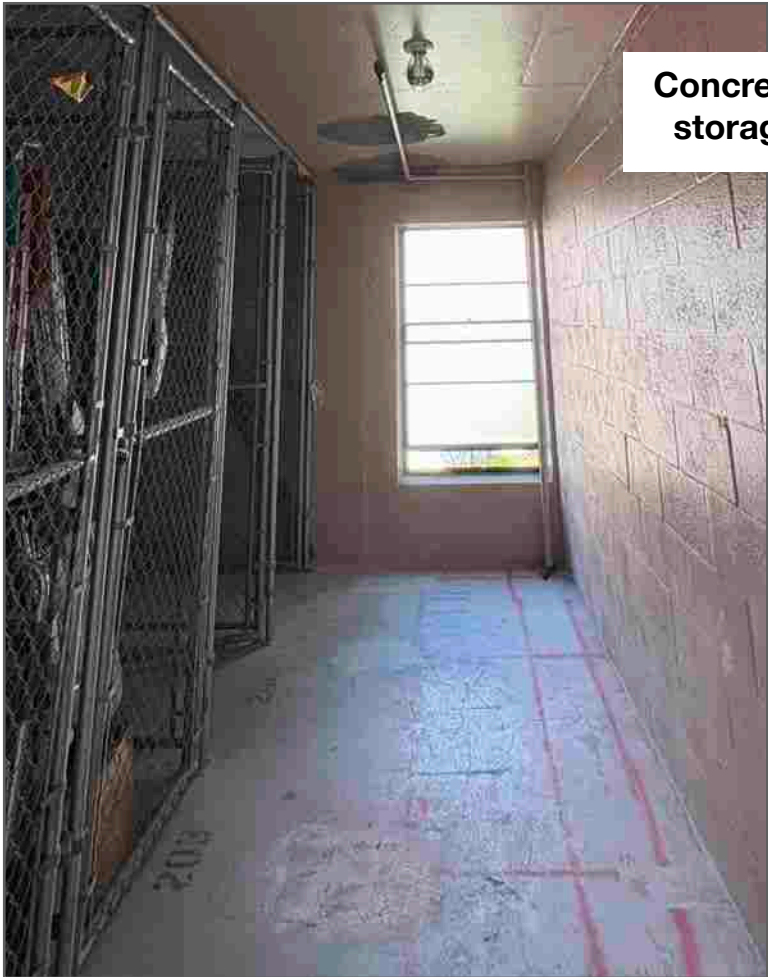

Concrete pours
storage units

