



"Everything in Excellence"

WILLIAMS & THOMAS CONSTRUCTION CO.

4473 Progress Ave., Ste 1, Naples, FL 34104

561.460.8525 | www.wtconstruct.com | CGC1532780

WEEKLY PROGRESS REPORT

Report No.	Date
#45	06/26/26

CLIENT:

Huntington Lakes IV

7320 Amberly Lane, Delray Beach, FL 33446

Attn: Nici Mahlandt | 201-936-9377

Email: nmahlandt@hotmail.com

OWNER'S REP:

Hellas Engineering

2475 Mercer Ave. Suite 106, West Palm Beach, Florida 33401

Contact: Austin Brennen 561-469-1907/561-348-4700

Email: austin@hellaseng.com

PROJECT: BUILDING RESTORATION PROJECT – HUNTINGTON LAKES IV

WEEK ENDING JUNE 26, 2026

June 22

1. Repaired screen enclosure on tile; **unit 306 BLDG 30**
2. Installed control joints on **BLDGs 30 and 31**
3. Poured concrete to close partial depth on **BLDG 30**
4. Opened slab for installation of control joints on **BLDG 30/stack 6**

June 23

5. Installed window bucking in two windows **BLDG 29 unit 310**
6. Installed dens glass **BLDG 30, unit 205**
7. PT edge repair **BLDG 32 by elevator**

June 24

8. Installed windows in unit **310 BLDG 29**
9. Cleaned PT pockets and added grout **stacks 1 and 2 BLDG 30**
10. Installed plywood (waterproofing) on exterior of **Unit 101 BLDG 30**

June 25

11. Installed Dens Glass **BLDG 29. Stack 10 210/110**
12. Installed bucking in bathroom window **BLDG 29 Unit 410**
13. Began work on **BLDG 29 units 109 and 309**

June 26

14. Edge Repair on **BLDG 32** ready for inspection
15. Installed dust wall **BLDG 29 unit 308**
16. Cut stucco(exterior) **BLDG 29 unit 308 and 109**
17. Installed bucking for window **BLDG 29 unit 309**
18. Stucco'd stack 1 **BLDG 31**
19. Scans taken to locate PT cables **BLDG 29**

**Expected
Progress week
of 6/29/26**

**Completion of control
joint installations
Building 30 and Stack
1 BLDG 29**

**Post Tension cable
repairs on BLDG 29**

**Post Tension Cable
repairs on BLDG 32
by elevator**

Railing picket repairs


**Window installs,
BLDG 29**

**BLDG 29 lanai
inspections**

**Crack repairs on
BLDG 30 410**

WEEKLY PROGRESS REPORT – SUMMARY DETAILS

WORK DAYS	WEATHER DELAYS	Holiday	AVG. DAILY MANPOWER	BLDGS WORKING ON
5	0	0	10-13	30/31/29/32



"Everything in Excellence"

WILLIAMS & THOMAS CONSTRUCTION CO.

4473 Progress Ave., Ste 1, Naples, FL 34104


561.460.8525 | www.wtconstruct.com | CGC1532780


WEEKLY PROGRESS REPORT

Report No.	Date
#45	06/26/26



**Bad framing on
building 29 windows**

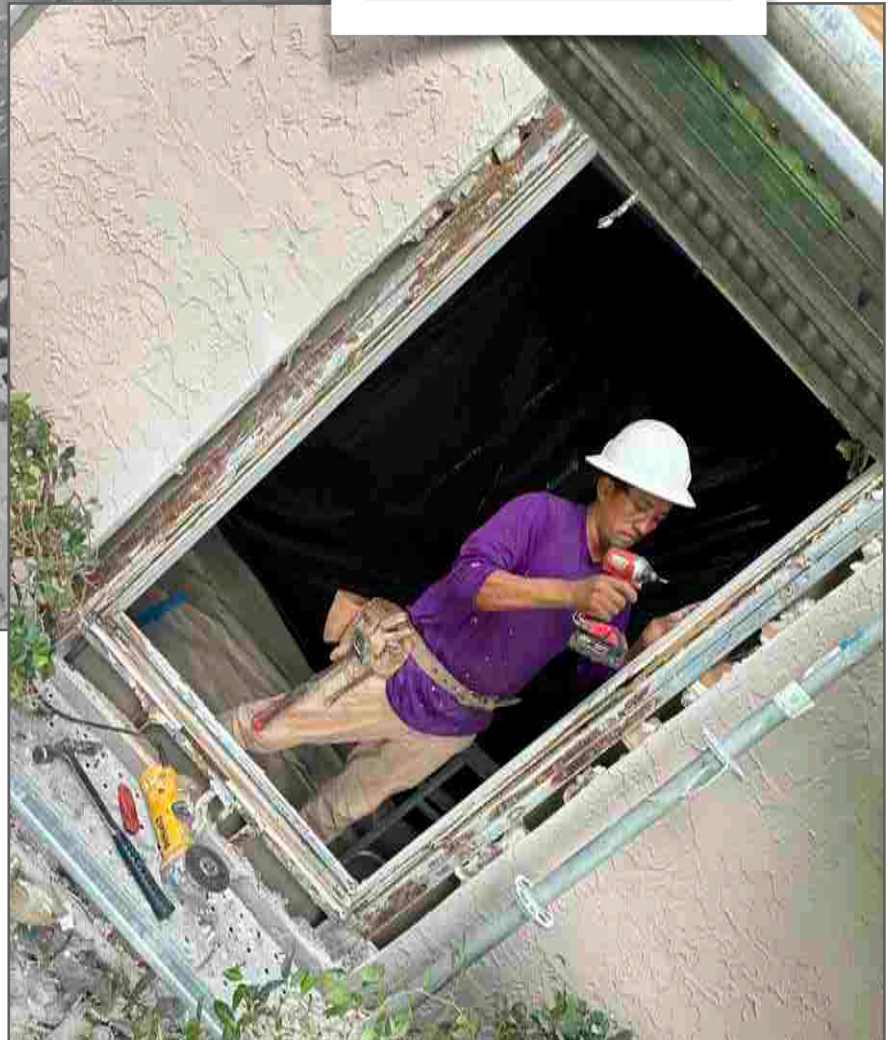



WILLIAMS & THOMAS CONSTRUCTION CO.
4473 Progress Ave., Ste 1, Naples, FL 34104
561.460.8525 | www.wtconstruct.com | CGC1532780

WEEKLY PROGRESS REPORT

Report No.	Date
#45	06/26/26



**Stucco Building
31...One Stack**



**Window prep,
BLDG 29**



"Everything in Excellence"

WILLIAMS & THOMAS CONSTRUCTION CO.

4473 Progress Ave., Ste 1, Naples, FL 34104


561.460.8525 | www.wtconstruct.com | CGC1532780

WEEKLY PROGRESS REPORT

Report No.	Date
#45	06/26/26



**Building 32
PT work**

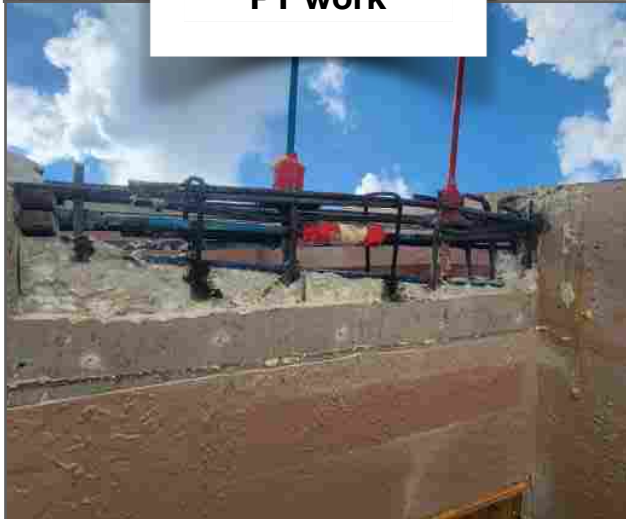

**Control Joint
Installation**
