



"Everything in Excellence"

WILLIAMS & THOMAS CONSTRUCTION CO.

4473 Progress Ave., Ste 1, Naples, FL 34104

561.460.8525 | www.wtconstruct.com | CGC1532780

WEEKLY PROGRESS REPORT

Report No.	Date
#47	07/10/26

CLIENT:

Huntington Lakes IV

7320 Amberly Lane, Delray Beach, FL 33446

Attn: Nici Mahlandt | 201-936-9377

Email: nmahlandt@hotmail.com

OWNER'S REP:

Hellas Engineering

2475 Mercer Ave. Suite 106, West Palm Beach, Florida 33401

Contact: Austin Brennen 561-469-1907/561-348-4700

Email: austin@hellaseng.com

PROJECT: BUILDING RESTORATION PROJECT – HUNTINGTON LAKES IV

WEEK ENDING JULY 10, 2026

July 06

1. Painted Stack 6 on **Building 30**.
2. Began window bucking at Unit 104
3. Started work on Unit 103.
4. Removed dust walls from Units 310, 210, and 110.

July 7

5. Installed window bucks/windows at **Building 29 Units 103, 104, and 306**.
6. Removed dust wall at **Building 30 Unit 101** and completed insulation installation.
7. Completed trash cleanup. Moved dumpster to other side of parking lot
8. Moved scaffolding on **Building 29**.

July 8

9. Removed dust walls at Units 103, 104, and 306.
10. Installed dens glass, units 103, 104, 306.
11. Built a dust wall at Unit 406 and cut the exterior wall to inspect frame bucking (no window installed yet).
12. Fully painted Stack 1 on **Building 31**.

July 9

13. Cables stressed on **Building 32**
14. Installed windows in units 205, 406, 405 **Building 29**.

July 10

15. Poured concrete for post tension pockets **Building 32 (ready for paint)**
16. Window bucking installed for windows 204 and 304 **Building 29**

**Expected
Progress week
of 7/13/26**

**Pre-inspection lanai
walkthroughs with
BLDG 29 Captain**

**Engineer inspections
of BLDG 29 Lanais**

**Post Tension Cable
Replacements on
BLDG 29**


**Installation of
remaining jalousie
replacement windows,
BLDG 29**

**Punch list BLDGS
32 and 31**

**Post Pocket Railings
BLGD 30**

WEEKLY PROGRESS REPORT – SUMMARY DETAILS

WORK DAYS	WEATHER DELAYS	Holiday	AVG. DAILY MANPOWER	BLDGS WORKING ON
5	0	0	10-13	30/31/29/32



"Everything in Excellence"


WILLIAMS & THOMAS CONSTRUCTION CO.

4473 Progress Ave., Ste 1, Naples, FL 34104


561.460.8525 | www.wtconstruct.com | CGC1532780

WEEKLY PROGRESS REPORT

Report No.	Date
#47	07/10/26

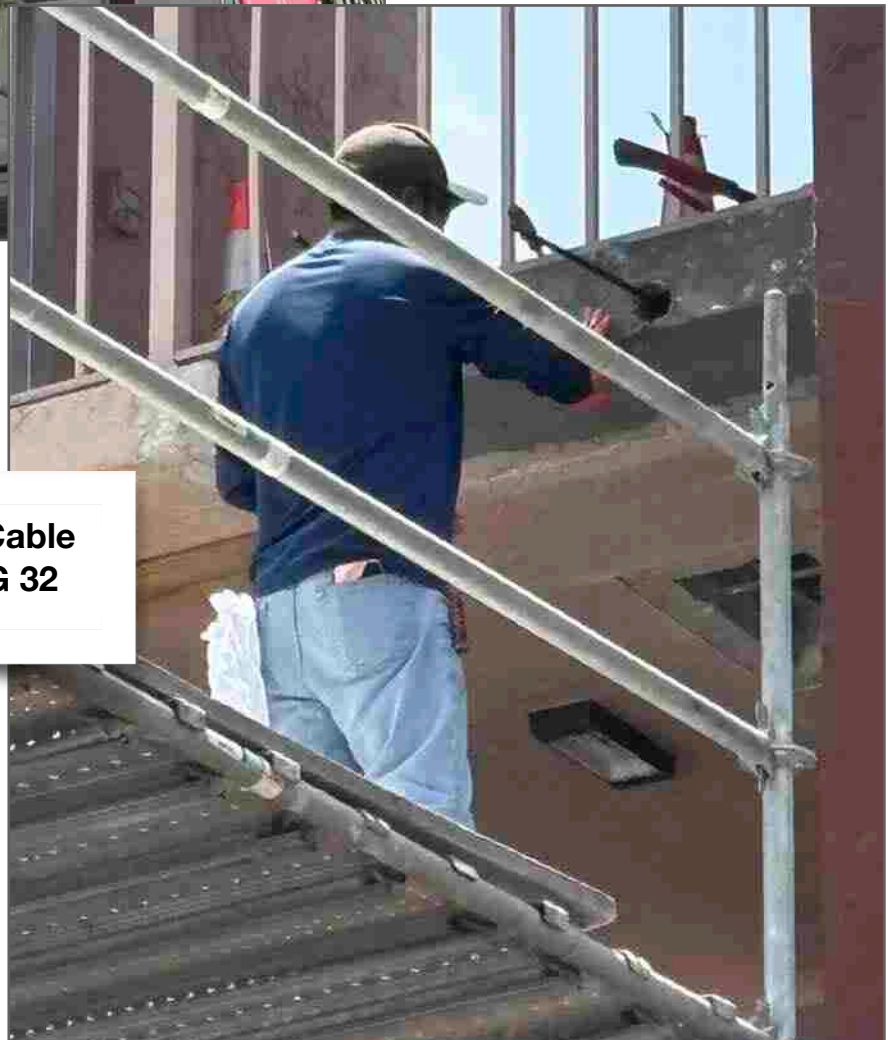

**Post Tension Cable
Repairs BLDG 32**



"Everything in Excellence"

WILLIAMS & THOMAS CONSTRUCTION CO.

4473 Progress Ave., Ste 1, Naples, FL 34104

561.460.8525 | www.wtconstruct.com | CGC1532780


WEEKLY PROGRESS REPORT

Report No.	Date
#47	06/26/26

**Painting
complete stack 1
BLDG 31**



**Painting
complete stack
10 BLDG 30**

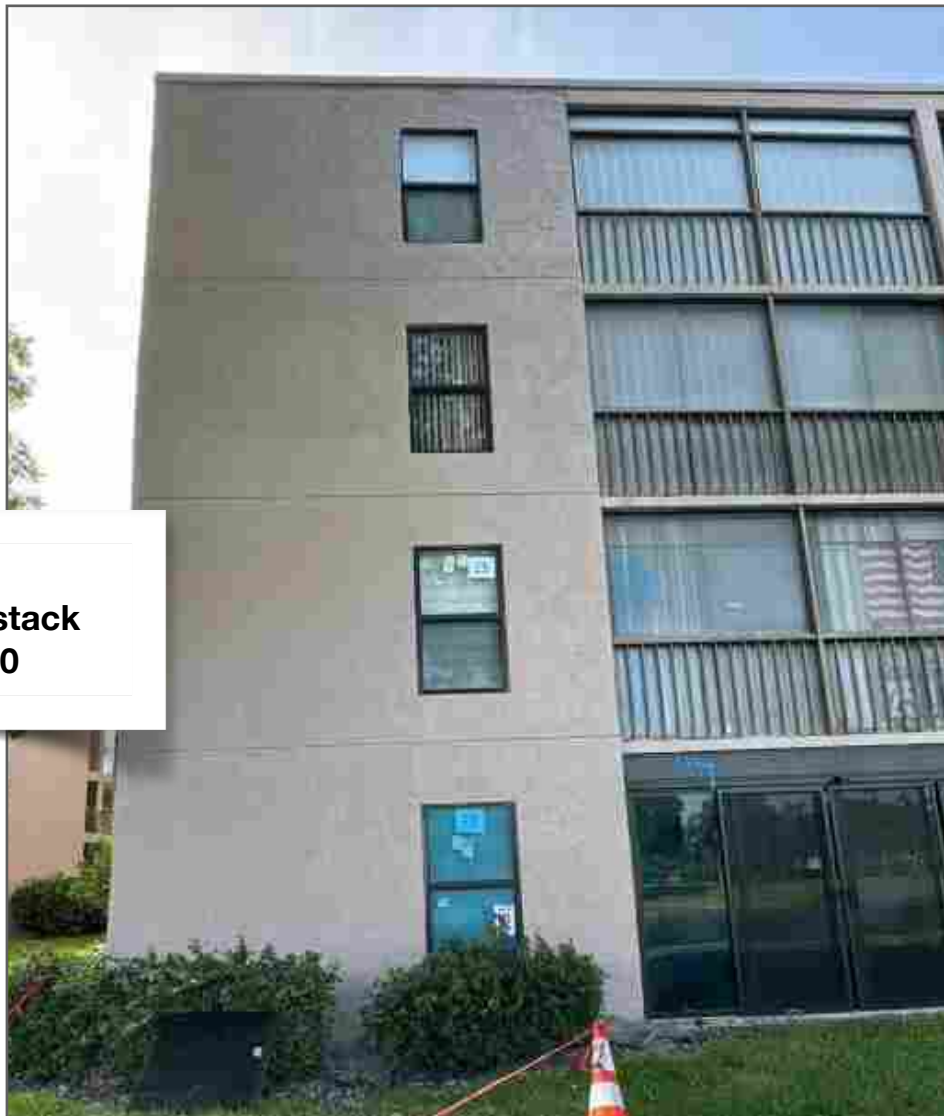



"Everything in Excellence"

WILLIAMS & THOMAS CONSTRUCTION CO.

4473 Progress Ave., Ste 1, Naples, FL 34104
561.460.8525 | www.wtconstruct.com | CGC1532780

WEEKLY PROGRESS REPORT

Report No.	Date
#46	07/10/2026



**Window installs
BLDG 29**
