



"Everything in Excellence"

WILLIAMS & THOMAS CONSTRUCTION CO.

4473 Progress Ave., Ste 1, Naples, FL 34104

561.460.8525 | www.wtconstruct.com | CGC1532780

WEEKLY PROGRESS REPORT

Report No.	Date
#48	07/17/26

CLIENT:

Huntington Lakes IV

7320 Amberly Lane, Delray Beach, FL 33446

Attn: Nici Mahlandt | 201-936-9377

Email: nmahlandt@hotmail.com

OWNER'S REP:

Hellas Engineering

2475 Mercer Ave. Suite 106, West Palm Beach, Florida 33401

Contact: Austin Brennen 561-469-1907/561-348-4700

Email: austin@hellaseng.com

PROJECT: BUILDING RESTORATION PROJECT – HUNTINGTON LAKES IV

WEEK ENDING JULY 17, 2026

July 13

1. Pre-inspection of lanais in building 29 (all floors)
2. Painted post pockets holes on building 32
3. Installed wood bucks on windows units 404 and 408
4. Boom lift returned

July 14

5. Dens Glass installed on windows/building 29
6. Applied stucco bldg 30/stack 1
7. Installed windows bldg. 29/ unit 210
8. Passed buck inspections units 404, 408, 204, 304, 110

July 15

9. Window bucks and windows installed units 203, 403 bldg., 29
10. Dust walls installed in five units, bldg,29

July 16

11. Interior repairs (stucco) in units on fourth floor, bldg. 29
12. Window installs
13. Scaffolding installed back of bldg., 29

July 17

14. Stucco'd lanais in bldg., 30 fourth floor
15. Installed backings bldg. 29 units 402, 302
16. Painted stairwell, bldg. 30
17. Scaffolding stack one, bldg. 29

**Expected
Progress week
of 7/20/26**

**Dust walls installed to
cover storage units
building 29 (3 floors)**

Punch 31

**Removing
scaffolding
bldg. 32**

**Relocating scaffolding
to balcony walls**

**Beginning scaffolding
on bldg 36**

**Eng. coming to
inspect lanai's blogs
30 and 29**

WEEKLY PROGRESS REPORT – SUMMARY DETAILS

WORK DAYS	WEATHER DELAYS	Holiday	AVG. DAILY MANPOWER	BLDGS WORKING ON
5	0	0	9-11	30/29/32


WEEKLY PROGRESS REPORT

Report No.

#48

Date

07/17/26

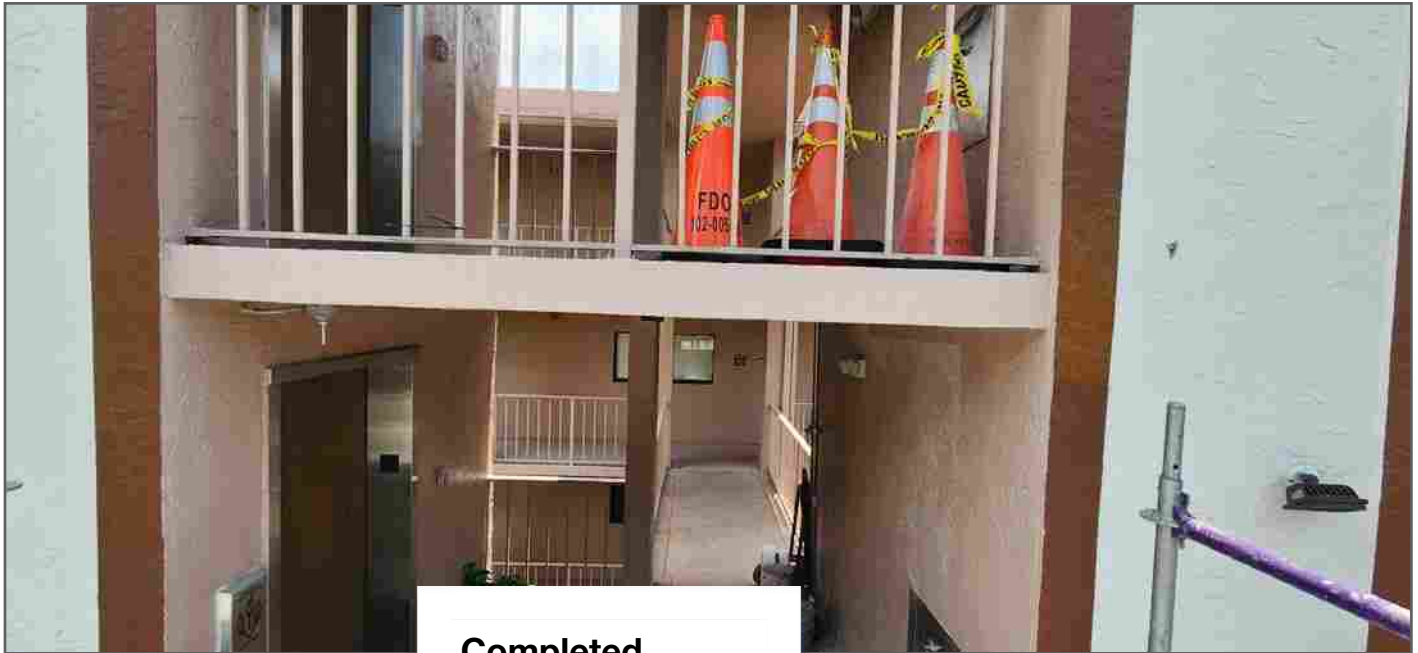

**Completed
painting on BLDG
32, PT Cable
replacement area**



**Dust walls
installed in
BLDG 29**





"Everything in Excellence"

WILLIAMS & THOMAS CONSTRUCTION CO.

4473 Progress Ave., Ste 1, Naples, FL 34104
561.460.8525 | www.wtconstruct.com | CGC1532780

WEEKLY PROGRESS REPORT

Report No.	Date
#48	07/17/2026



**Dens Glass installed
around windows**

**Scaffolding
installed on
one stack
bldg. 29**



Stucco work

